PHOTOVOLTAIC SYSTEMS

SCOTT COUNTY, IOWA



PV WORKSHEET – STANDARD STRING ARRAY

Solar photovoltaic (PV) systems have widely gained acceptance as an alternative energy source and installations range from the small array supplying a bus stop luminaire to a large array that covers acres. Since each installation comes with its own characteristics this worksheet has been provided for the installer to complete and submit to his/her electrical inspector for obtaining a permit. The entire PV system installation must comply with Article 690 of the 2014 National Electrical Code (NEC).

To obtain a permit please provide the following documentation to Scott County Planning & Development:

- 1. Pages 2, 3 and 4 of this document
- 2. Equipment spec/cut sheets for grounding/bonding fittings, modules, inverters, micro inverters, or optimizers (if these are not available complete page 4 of this document)
- 3. A one-line diagram of the PV system including service interconnection
- 4. A site plan showing the relative location of the array and the PV equipment on the property. Also provide location of service and distance from array.

A PV installer is allowed to construct the support system, mount the modules, inverters or optimizers, and connect the factory provided module wiring harness (plug and play). The remainder of the installation such as panelboards, raceways, boxes, fittings, breakers, and building wire shall be installed by a licensed electrical contractor.

PHOTOVOLTAIC SYSTEMS

SCOTT COUNTY, IOWA

PV SYSTEM INFORMATION

		TYPE OF ARRAY		
Υ	N		Υ	N
Roof Array?		Rapid Shutdown Required (690.12)?		
Ground Array?		Guarding of Conductors Required (690.31A)?		

PV SYSTEM OVERVIEW				
Maximum System Voltage	T			
#Modules/String				
#Strings in System				
Maximum Circuit Current				
Battery Storage? Y N				

LOAD SIDE CONNECTION ¹				
Service Voltage				
Service Panel Main Breaker				
Service Panel Bus Rating				
Service Conductor Size				
PV System OCPD2 Rating				

CALCULATIONS:

MAXIMUM SYSTEM VOLTAGE - 690.7(A);

(Voc) (module label) X Thermal Coefficient³ X # of modules/string = V_{MAX}

MAXIMUM CIRCUIT CURRENT – 690.8(a)(1):

(Isc)(module label) X (Sum of the paralleled modules) X 125%=IMAX

OVERCURRENT DEVICE RATING - 690.9(B):

(Imax) $X 125\% = OCPD^2$

¹Supply side connections may be allowed by your utility and shall comply with 705.12(A)


²OCPD - Overcurrent Protective Device

PHOTOVOLTAIC SYSTEMS

SCOTT COUNTY, IOWA



CONDUCTOR AND RACEWAY SCHEDULE

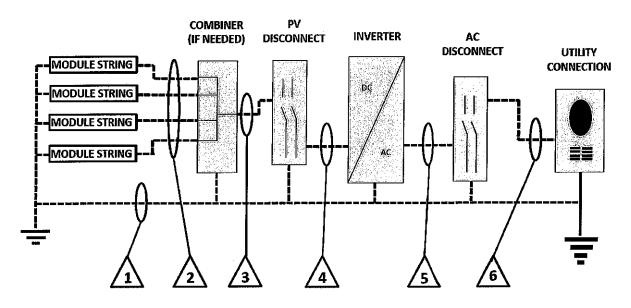

Δ	Conductor Type	Conductor AWG	Conduit Type NA	Conduit Size	
1	Copper Grounding Electrode Conductor Copper Equipment Grounding Conductor			NA	
2	PV Source Conductors Use -2 PV Wire		NA	NA	
3	THWN-2 XHHW-2 RHW-2				
4	THWN-2 XHHW-2 RHW-2				
5	THWN-2 XHHW-2 RHW-2				
6	THWN-2 XHHW-2 RHW-2				
